



Monthly Reporting

Reporting Period: October 2020

Reference: MR/10/2020

Date: 10 November 2020



**GOVERNMENT OF THE
VIRGIN ISLANDS**
Premier's Office



**VIRGIN ISLANDS
RECOVERY AND
DEVELOPMENT AGENCY**

Email: feedback@bvirecovery.com
Website: www.bvirecovery.vg
First Floor, Ritter House,
Wickham's Cay II, Tortola VG1110, Virgin Islands

Table of Acronyms

BOQ	Bill of Quantities
BVI-EC	British Virgin Islands Electricity Corporation
BVIPA	British Virgin Islands Ports Authority
CDB	Caribbean Development Bank
DWM	Department of Waste Management
ITT	Invitation to Tender
GOVI	Government of Virgin Islands
JVD	Jost Van Dyke
MECYAFA	Ministry of Education, Culture, Youth Affairs, Fisheries & Agriculture
MEP	Mechanical, Electrical and Plumbing
MTWU	Ministry of Transportation, Works & Utilities
MHSD	Ministry of Health and Social Development
MNRLI	Ministry of Natural Resources, Labour and Immigration
NOC	National Oceanography Centre (UK)
RE	Renewable Energy
RDA	Recovery and Development Agency
RDP	Recovery to Development Plan
SoR	Statement of Requirement
SoW	Scope of Works
ToR	Terms of Reference
VISR	Virgin Islands Shipping Registry

Table of Contents

Table of Acronyms	3
Table of Figures	4
1. Project Status Updates – Phase One and RDP Projects	5
2. Project Status Updates – CDB Programme	11
3. Future Planning	13
3.1. Repair to Recreational Facilities	13
3.2. Repair to Other Judges residences	13
4. Communications	14
5. Funding	22
6. Project Updates – Phase One Programme	24
7. Project Updates – CDB Programme	34
8. Completed Projects	42
8.1. Past Completed Projects	43

Table of Figures

Table 1: Projects Currently in Planning Phase	5
Table 2: Projects Currently in Procurement Phase	5
Table 3: Projects Currently in Delivery Phase	6
Table 4: Projects Completed	7
Table 5: Projects on Hold	9
Table 6: Projects Cancelled	9
Table 7: Projects Currently in Planning Phase	11
Table 8: Projects Currently in the Procurement Phase	11
Table 9: Events and Communications in October	14
Table 10: Contracted Contributions by Project and Amount Contracted	22

Date	Description
10 November 2020	First draft report completed
19 November 2020	First draft approved by RDA Board
4 December 2020	First draft sent to Office of Premier for review
12 January 2021	RDA receives feedback from Office of Premier
13 January 2021	RDA finalises and publishes the report

1. Project Status Updates – Phase One and RDP Projects

Table 1: Projects Currently in Planning Phase

Project ID	Project Name	Lead Ministry	Status
122	Redevelopment of Elmore Stouff High School	Education, Culture, Youth Affairs, Fisheries & Agriculture	The Ministry has signed off on the Statement of Requirements prepared by the Construction for Change (CfC) consultant and agreed a new budget to meet the increased scope.
177	Marine Base	Governor's Group	Completion of the removal of derelict cars and unnecessary vessels from the site will be necessary prior to procurement and commencement of works. Potential funding for design works, fencing and boat storage has been offered.
541	Rehabilitation of Jost Van Dyke Primary School	Education, Culture, Youth Affairs, Fisheries & Agriculture	In July a community meeting was held to discuss the school refurbishment. The community is overwhelmingly in favour of a new site being selected for the school, so a cost benefit analysis of the options is required. As such an updated SoR has been signed off by the Ministry. A meeting with the Ministry is scheduled for early November to discuss forward direction of this project and costing of the new site option.
660	Expanded Sewerage	Transportation, Works & Utilities	This project aims to improve and expand the national sewerage system across both Tortola and sister islands. A procurement strategy is being finalized, as well as specific location reviews, and procurement documentation reviews. In September the inception report was completed and submitted to the Ministry for review. This report is awaiting feedback from the Ministry.

Table 2: Projects Currently in Procurement Phase

Project ID	Project Name	Lead Ministry	Status
163	Repair Anegada Police Station	Governor's Group	The ITT for this project was issued on 22 September and returns were due on 28 October. A site visit and bidders' conference

			to facilitate the procurement process was held on 2 October. At the end of October, tender returns had been received and were under evaluation.
193	Attorney General's & Judges Residence Rehabilitation	Governor's Group	An ITT was issued for repair of the AG's residence on 22 September, with returns due by 26 October. A site visit and bidder's conference was held on 25 September during which contractors toured the damaged building, facilitating preparation of bids. Tender returns have now been received and are under evaluation following which a contractor will be selected. Further planning and construction of the three Judges' residences will await funding.

Table 3: Projects Currently in Delivery Phase

Project ID	Name	Lead Ministry	Status
151	Virgin Gorda Sports Complex	Education, Culture, Youth Affairs, Fisheries & Agriculture	<p>Works to complete installation of windows, court flooring and lights continued in October, now scheduled to be completed in November, bringing phase one of this project to a close.</p> <p>Works on the restroom facilities under phase 2 of this project continued in October, and this activity is scheduled to be completed in March 2021.</p>
152	AO Shirley Grounds Phase One	Education, Culture, Youth Affairs, Fisheries & Agriculture	<p>Grandstand: The gym area is being focused on for completion. The gym area roof, handrails and staircases have all been installed. The seating has arrived and is being installed, to be followed by painting. This activity is now scheduled to be completed in November, partly due to delays caused by the COVID curfew.</p> <p>Lighting: In October, the delayed lighting for the grounds arrived, and installation of these lights is expected to start in November.</p> <p>Pavilion: This activity is on hold. Further progress depends on finalisation of the new requirement and confirmation of availability of additional resources by the MECYFA.</p>

Project ID	Name	Lead Ministry	Status
181	Repair of Road Town Police Station	Governor's Group	In October, funding was confirmed and deeds of contribution signed by both the Virgin Islands and UK Governments. October also saw award and signature of the construction contract and the commencement of works. Construction is scheduled to be completed within the next few months.
189	Marine Survey	Natural Resources, Labour & Immigration	<p>Computers arrived on 30 December 2019; water quality equipment was delivered on 9 January 2020; and final Ferritech equipment was received. Equipment was handed over to the Ministry on 7 February 2020.</p> <p>The UK National Oceanography Centre is expected to undertake stakeholder engagement, assessment of data and scientific products, and deliver additional training. There were plans for UK NOC to visit in March, however this was postponed by MNRLI. This visit will most likely be rescheduled to November 2020. Until then, remote work and training methods will be utilised.</p> <p>As of June, the close out report for completed activities has been finalised and a follow up meeting is being held between UK NOC and MNRLI.</p> <p>The team is currently reviewing the feasibility of remote stakeholder engagements as well as possibly applying for further funding.</p>

Table 4: Projects Completed

Project ID	Name	Lead Ministry	Status
103	Virgin Gorda Baths	Natural Resources, Labour & Immigration	The project was completed with Maynard Construction on 22 January 2020. The handover certificate was signed off on 6 May.
108	Special Debris Clearance	Health & Social Development	The project is complete. In June 2019, the final activity budget was reconciled, and a closure report completed. The final Value for Money report has been published on the RDA website.

Project ID	Name	Lead Ministry	Status
136	Sea markers	Transportation, Works & Utilities	The final sea markers were installed on 12 May, finalising this project. The Shipping Registry (VISR) has formally signed off this project as complete.
145	Bregado Flax Junior School Improvements	Education, Culture, Youth Affairs, Fisheries & Agriculture	The main works were completed in early January. There was a variation to the contract issued to paint the floors, which was completed on 27 January. Fire escape doors were completed in August 2020, bringing this project to full completion.
146	ESHS Demolition	Education, Culture, Youth Affairs, Fisheries & Agriculture	The closeout report for this project has been finalised. The Value for Money evaluation has been completed and the report has been published.
147	Elmore Stoutt High School	Education, Culture, Youth Affairs, Fisheries & Agriculture	The temporary modular units arrived on Tortola on 18 August 2019 and were commissioned as music classrooms for the Advent School Term in September 2019. The CTL building refurbishment project was completed and turned over to the Ministry also for the Advent School Term. The VfM reports on two activities within this project have been published.
154	Temporary housing	Health & Social Development	This project was handed back to the Ministry on 3 March 2020. There is one home that still requires utility connections on Tortola.
157	Repair to damaged homes	Health & Social Development	Repairs for the first home on Virgin Gorda have been completed. The remaining identified homes have been handed back to the Ministry for their action.
160	Repair VG Admin Building – WaltSCO Building	Governor's Group	RDA was requested to perform a second industrial deep clean to the WaltSCO Building. The cleaning was completed in December 2019 and a completion certificate was delivered on 8 January. Procurement of the repair of the Vanterpool and Flax Admin Buildings is underway by the RDA drawing on CDB Rehabilitation and Reconstruction Loan funding.
182	Virgin Gorda Police Barracks	Governor's Group	Official handover of the VG Barracks took place on 5 September 2019.

Project ID	Name	Lead Ministry	Status
			A project closeout report has been drafted and is in circulation. The VfM Report has also been published on the RDA website.
183	Jost Van Dyke Admin Building	Governor's Group	All works have been completed and the project transferred back to GoVI. The official opening and naming ceremony for the building was held on 20 December 2019. The VfM Report has been published on the RDA website.
187	Dismantling of old incinerator	Health and Social Development	Removal of the incinerator is complete. All other works on the site were completed on 29 May. A close out report has been drafted and is being finalised.

Table 5: Projects on Hold

Project ID	Name	Lead Ministry	Status
133	Removal of derelict boats	Natural Resources, Labour & Immigration	For the Nanny Cay pilot for this project, the final bins of fiberglass have been removed from the Paraquita Bay site to the Waste Management site in Pockwood Pond. Given expiry of the tender validity period for this project in mid-November, this project has been placed on-hold.
179	VHF network analysis and build	Governor's Group	This project is currently on hold.
186	Installation of incinerator scrubber	Health and Social Development	Agreement with MHSD for the RDA to move this project forward. Technical details of the incinerator to be reviewed once detailed plans provided by MHSD.
188	Designs for new incinerator	Health and Social Development	Agreement with MHSD for the RDA to move this project forward. Technical details of incinerator to be reviewed in coming weeks, once detailed designs are provided by MHSD.

Table 6: Projects Cancelled

Project ID	Name	Lead Ministry	Status
104	Sage Mountain Restoration	Natural Resources, Labour & Immigration	It has been agreed that this project will be completed by National Parks Trust and not RDA.
119	Prospect Reef Hotel Wall	Premier's Office	This project has been cancelled at request of Government in January 2019.

124	Cane Garden Bay dinghy dock repair	Premier's Office	It has been agreed in January 2019 that this project will be completed by the Office of the Premier and not the RDA.
126	Long Bay bathroom, stalls, and shades	Transportation, Works & Utilities	This project has been cancelled, as MCW completed the temporary facilities.
134	Above/below water debris clearance	Natural Resources, Labour & Immigration	Project cancelled at request of MNRLI in January 2019.
135	Debris Site Fence Repairs	Natural Resources, Labour & Immigration	Project cancelled at request of BVIEC in June 2019.
149	School Furniture and Equipment	Education, Culture, Youth Affairs, Fisheries & Agriculture	Cancelled at request of MoF Projects Unit, as enough school supplies are already being purchased by MoF under the CDB RRL.
150	TA team - Education Strategy	Education, Culture, Youth Affairs, Fisheries & Agriculture	Cancelled by Permanent Secretary and confirmed at January 2019 workshop.
155	Social registry system development	Health & Social Development	Cancelled at the January 2019 workshop.

2. Project Status Updates – CDB Programme

Several projects that are part of the Caribbean Development Bank (CDB) Programme, funded by the Rehabilitation and Reconstruction Loan (RRL) have been handed over to the RDA for implementation in conjunction with Central Government. A new section in status updates has thus been created to report on their progress.

Table 7: Projects Currently in Planning Phase

Project ID	Project Name	Lead Ministry	Status
060	Magistrates Court	Governor's Group	Deputy Governor's Office's approval of the Inception and Environmental and Social Management reports was secured in late September. In October, RDA held discussions with the design consultant Trojan and the DGO on scaling the project requirements based on the available budget. This will need to be agreed prior to procurement of construction.
083	Eslyn Henley Richez Learning Centre	Education, Culture, Youth Affairs, Fisheries & Agriculture	The Ministry has confirmed agreement with the recommended option presented in the final Inception Report, and the consulting firm has been instructed to proceed with the preliminary design based on the recommended option. In October several environmental issues were highlighted which will be incorporated in the preliminary design.
091	West End Ferry Terminal	Premier's Office	The evaluation report for the Expressions of Interest (EOI) for the Consultant who will oversee the project has been submitted to the CDB for its no objection, following which a contract will be issued to the selected firm.

Table 8: Projects Currently in the Delivery Phase

Project ID	Project Name	Lead Ministry	Status
086	Bregado Flax Education Centre	Education, Culture, Youth Affairs, Fisheries & Agriculture	In October the steel formwork and concrete pouring for one of the classroom building's roof was completed. The contractor's proposed variations have been submitted and are currently under review.
140	Reservoirs and Metering	Transportation, Works & Utilities	Autland Construction is proceeding with site work on two sites, with a 30-day contract extension granted due to weather and COVID-19 delays. Carrot Bay site: Progress has continued on site and both the upper and lower concrete

			<p>retaining walls have been completed and backfilled.</p> <p>Long Bush site: The steel and concrete work for the lower section of the retaining wall is in progress.</p> <p>Zion Hill site: The current reservoir must remain in full operation until the Carrot Bay reservoir has been constructed, tested and commissioned. This was not envisioned at the start of the project but is the only way to ensure water supply to local residents is not interrupted.</p>
180	Roads, Slopes, and Coastal Defences	Transportation, Works & Utilities	<p>Site work on the Great Mountain 1 site continued in October. The retaining wall including weep holes and geotextile fabric has been completed and backfilled. Four contract signings for this project were held in October, namely the Great Mountain 2 site, the Ballast Bay/Windy Hill site, Bob's Gas Station, and Little Dix Hill. The final two packages will be initiated once the preceding works are completed, in order to ensure traffic flow into and out of Road Town is maintained.</p>
200	Other Government Buildings	Transportation, Works & Utilities	<p>Work continues on both the Flax and North Sound contracts.</p> <p>Work on the Flax Building contract remains on track despite some COVID-19 delays. The new roof has been installed, and drywall, electrical work and tiling work is nearing completion.</p> <p>The North Sound Building works are progressing, now scheduled to be completed by the end of November, following COVID-19 delays.</p> <p>The Vanterpool building contract was signed on 15 October, and the contractor is expected to have full access to the building from 15 November.</p>

3. Future Planning

The RDA is working on a range of recovery and development projects across the Virgin Islands. The section below details projects currently in planning that have not been fully approved with a signed SoR from Central Government. Once a project has a signed SoR, the project will move to the Project Updates section of this report. Once a project is complete, a summary of the project can be found in the Completed Projects section at the end of the document.

Current future projects in planning include:

3.1. Repair to Recreational Facilities

The RDA is working with the Ministry of Education, Culture, Youth Affairs, Fisheries and Agriculture (MECYFA), the Recreation Committee and the NGO, Unite BVI to repair two recreational facilities on Anegada and Tortola. The next steps are to develop a concept note, conduct a cost estimate, confirm with Central Government that the project is a priority, and source additional funds as needed. Each project has estimated costs that are beyond the donations that have already been received. Initial planning is underway, however further planning and construction will begin when funding becomes available.

3.2. Repair to Other Judges residences

Working with the Deputy Governor's Office to rekindle the refurbishment of the other three properties in the Macnamara Estate, the RDA has provided rough-order magnitude cost estimates to the Deputy Governor's Office to inform decisions regarding funding. This project is currently unfunded.

4. Communications

This section reviews key events and communications releases.

Table 9: Events and Communications in October

Events	Date	Description
Contract Signing – Repairs Works to Road Town Police Station, Ballast Bay Slope Stabilization and Road Rehabilitation and Great Mountain II Slope Stabilization and Road Rehabilitation Works	5 October	K and C Construction was awarded the contract for repairs to Road Town Police Station valued at \$245, 520.09, the first joint venture was awarded for the Ballast Bay Slope Stabilization and Road Rehabilitation to Autland and STO Enterprises valued at \$1,054,125.93 and Autland Heavy Equipment was awarded the contract for Great Mountain II valued at \$447,461.30.
Community Meeting Hope Hill to Sabbath Hill Road Rehabilitation and Slope Stablisation	8 October	Team RDA joined by Government Ministers led a community-based meeting for residents of Hope Hill to share project details for upcoming Road Works and traffic diversions for the Hope Hill to Sabbath Hill Road Rehabilitation and Slope Stablisation Project.
Deed of Contribution Signing Ceremony with BVI and UK Governments for Road Town Police Station and Design Phase of the Magistrates Court	12 October	\$70k from Govt of VI and an additional \$70K from FCDO for Road Town Police Station plus \$187.5k for Magistrates Court from FCDO was signed over to the RDA for this Deed of Contribution Signing Ceremony.
CONTRACT SIGNING CEREMONY Little Dix Hill Slope Stabilization and Road Rehabilitation Works, Bob’s Gas Station Slope Stabilization and Road Rehabilitation Works and Repairs to the Vanterpool Administration Building	15 October	Caribbean Environmental Restoration Limited was awarded the contracts for the Little Dix Hill and Bob’s Gas Station Slope Stabilization and Road Rehabilitation Works valued at \$407,105.60 and \$494,308.10 respectively while Metro Construction was awarded the contract to repair the Vanterpool’s Administration Building valued at \$1,410,670.79.
Community Meeting Little Dix Hill, Hope Hill to Sabbath Hill to Hope Hill and Bob’s Gas Station	22 October	Community Meeting for the Residents of the East End, Long Look area in relation to the Little Dix Hill, Hope Hill to Sabbath Hill to Hope Hill and Bob’s Gas Station at the Willard Wheatley Primary School.
RDA Contractor Workshop	28 & 29 October	Over two days, 22 contractors attended the RDA Contractor Workshop at the RDA Office on Tortola.
Contract Signing Ceremony Deed of Contribution – Music Instruments for ESHS	30 October	Private Company, Maples BVI as part of their ongoing commitment to Music Education

		donated \$28K at a Deed of Contribution Signing Ceremony to purchase Steel Pans.
--	--	--

Videos	Date	Description
Contractor's Feedback from RDA Bidder's Conference for the Repairs to the AG's Residence	1 October	Several contractors provided positive feedback on the knowledge gained at the RDA Bidder's Conference for the Repairs to the AG's Residence
Video Announcement /Second Site Visit – Repair to AG's Residence	5 October	Video Announcement /Second Site Visit – Repair to AG's Residence
GIS Live Stream – Contract Signing – Repairs Works to Road Town Police Station, Ballast Bay Slope Stabilization and Road Rehabilitation and Great Mountain II Slope Stabilization and Road Rehabilitation Works	5 October	GIS Live Stream – Contract Signing – Repairs Works to Road Town Police Station, Ballast Bay Slope Stabilization and Road Rehabilitation and Great Mountain II Slope Stabilization and Road Rehabilitation Works
GIS Live Stream – Contract Signing – Deed of Contribution (BVI GOV and UK GOV) Road Town Police Station and Design Phase of the Magistrates Court	12 October	GIS Live Stream – Contract Signing – Deed of Contribution (BVI GOV and UK GOV) Road Town Police Station and Design Phase of the Magistrates Court
GIS Live Stream – Contract Signing – Little Dix Hill Slope Stablisation & Road Rehabilitation Works, Bob's Gas Station Slope Stablisation & Road Rehabilitation and Vanterpool Administration Building	15 October	GIS Live Stream – Contract Signing – Little Dix Hill Slope Stablisation & Road Rehabilitation Works, Bob's Gas Station Slope Stablisation & Road Rehabilitation and Vanterpool Administration Building

Social Media Posts	Date	Description
FLYER REPOST: Virgin Islands Recovery & Development Agency: Site Visit & Bidder's Conference – Repairs to the Anegada Administration Building	1 October	Caption: Friendly Reminder Site Visit & Bidder's Conference to repairs to the Anegada Administration Building on Anegada tomorrow. We will meet you at the Anegada Administration Building at 10:00am. See you there!!!
FLYER REPOST: Live Contract Signing Ceremony for Ballast Bay Road Rehabilitation & Slope Stabilisation, Great Mountain II Road Rehabilitation & Slope Stabilisation and Road Town Police Station Repair Works	5 October	FLYER REPOST: Live Contract Signing Ceremony for Ballast Bay Road Rehabilitation & Slope Stabilisation, Great Mountain II Road Rehabilitation & Slope Stabilisation and Road Town Police Station Repair Works
Contract Signing – Repairs Works to Road Town Police Station, Ballast Bay Slope Stabilization and Road Rehabilitation and Great Mountain II Slope Stabilization and Road Rehabilitation Works	5 October	Caption: As we are now in the fourth quarter of 2020, the RDA continues to implement and push its primary mandate, recovery. Today three contracts focused on rebuilding critical infrastructure were awarded to three local firms.

		<p>K&C Construction has been awarded the contract for repairs to the Road Town Police Station valued at US\$245,520.09. The contract for the Ballast Bay Slope Stabilization and Road Rehabilitation Works valuing US\$1,054,125.93 has been awarded to our very first joint venture between STO Enterprises Ltd and Autland Heavy Equipment Co. Ltd. And lastly, the Great Mountain II Slope Stabilization and Road Rehabilitation Works valuing US\$447,461.30 has been awarded to Autland Heavy Equipment Co. Ltd. We here at the RDA are proud partners of the Government of the Virgin Islands and it's our pleasure to work to serve the people of this territory.</p>
<p>REPOST: Contract Signing – Repairs Works to Road Town Police Station, Ballast Bay Slope Stabilization and Road Rehabilitation and Great Mountain II Slope Stabilization and Road Rehabilitation Works</p>	<p>5 October</p>	<p>CAPTION: Today, the Governor joined Ministers and District Representatives at a Contract Signing Ceremony for three important infrastructure projects - the Road Town Police Station, the Ballast Bay Road and the Great Mountain Road.</p> <p>The Governor paid tribute to the Virgin Islands Recovery & Development Agency (who will be leading the projects) for their work to help BVI build back better, in partnership with the local community as we respond to COVID-19. Local contractors will be taking forward the projects, appointed through free and fair competition to ensure the best possible results for BVI.</p> <p>The Road Town Police Station (co-funded by the UK Government) will provide critical improvements to the Royal Virgin Islands Police's facilities so they can perform their jobs to the highest standard.</p> <p>The Governor thanked all contractors, the RDA, the Government of the Virgin Islands and the Deputy Governor's Office for all their work to date.</p>
<p>INVITATION: Community Meeting Hope Hill to Sabbath Hill Road Rehabilitation and Slope Stabilisation</p>	<p>6 October</p>	<p>INVITATION: Community Meeting Hope Hill to Sabbath Hill Road Rehabilitation and Slope Stabilisation</p>

REPOST: Statement by Premier Fahie at Contract Signing - The BVI is in Transformation Mode	6 October	CAPTION: We continue to be pleased as a Government to renegotiate some of the terms in the Caribbean Development Bank's Rehabilitation and Reconstruction Loan when we took office in 2019... Click here to read more https://bit.ly/34x
FLYER REPOST: Bulletin Community Meeting for Residents of Hope to Sabbath Hill	6 October	FLYER REPOST: Bulletin Community Meeting for Residents of Hope to Sabbath Hill
FLYER: Tips for Tendering	7 October	New Tender Opportunity - Repairs to Attorney General's Residence. For more details click here: https://bit.ly/3cqwqyH
REPOST INVITATION: Community Meeting Hope Hill to Sabbath Hill Road Rehabilitation and Slope Stablisation (Reminder)	7 October	REPOST INVITATION: Community Meeting Hope Hill to Sabbath Hill Road Rehabilitation and Slope Stablisation (Reminder)
FLYER: RDA Contractor Workshop	8 October	CAPTION: Happy Friday Contractors!!!! We here at the RDA are excited to announce our upcoming Contractor Workshop which will be held on Tortola and Virgin Gorda in the coming weeks. Topics to be covered include: Construction and the Environment; Risk Management; Construction and the Community and so much more. To register email us at register@bvirecover.vg Seats are Limited so please do not hesitate to contact us today. This is one you do not want to miss
FLYER: RDA Contractor Workshop How to register.	12 October	FLYER: RDA Contractor Workshop How to register.
Contract Signing – Deed of Contribution (BVI GOV and UK GOV) Road Town Police Station and Design Phase of the Magistrates Court	12 October	Today is an exciting day at the RDA as we held a Deed of Contribution Signing Ceremony which displayed the partnership between the BVI Government, the UK Government and the RDA.

		<p>The first Deed of Contribution was for the receipt of funds from the BVI Government for the Road Town Police Station in the amount of \$70K.</p> <p>The UK Government matched that \$70K with a Deed of Contribution for the same, and in addition, contributed \$187,550 to the Design Phase of the Magistrates Court.</p> <p>Today was indeed a great day, not only for the RDA but for the territory of the Virgin Islands.</p>
FLYER: RDA Contractor Workshop	13 October	<p>Workshop Presenter: Tom Lilleyman Topic: Risk Management & Tips for Successful Tendering.</p>
CONTRACT SIGNING CEREMONY CONTRACT SIGNING CEREMONY Little Dix Hill Slope Stabilization and Road Rehabilitation Works, Bob's Gas Station Slope Stabilization and Road Rehabilitation Works and Repairs to the Vanterpool's Administration Building	15 October	<p>CAPTION: CONTRACT SIGNING CEREMONY Little Dix Hill Slope Stabilization and Road Rehabilitation Works</p> <p>Bob's Gas Station Slope Stabilization and Road Rehabilitation Works</p> <p>Repairs to the Vanterpool's Administration Building.</p> <p>As we continue on the road to recovery, today we signed 3 contracts for recovery works financed by the Government of the Virgin Islands through the CDB RRL.</p> <p>Caribbean Environmental Restoration Ltd was awarded two road projects today. They were awarded the contracts for Little Dix Hill Slope Stabilization and Road Rehabilitation Works which values \$407,105.60 and the Bob's Gas Station Slope Stabilization and Road Rehabilitation Works valuing \$494,308.10.</p> <p>Metro Construction Limited was awarded the contract for the Repairs to the Vanterpool' Administration Building valuing \$1,410,670.79.</p> <p>TeamWork makes the dream work. The RDA proudly partners with the Government of the Virgin Islands and together we will continue to work hard towards the recovery of these beautiful Virgin Islands.</p>

FLYER: RDA Contractor Workshop	15 October	Workshop Presenter: Patlian Johnson Topic: Construction and the Community
FLYER: Community Meeting Little Dix Hill, Hope Hill to Sabbath Hill to Hope Hill and Bob's Gas Station	16 October	CAPTION: The RDA will be hosting a Community Meeting addressing the present and upcoming road works in the East End, Hope Hill and Baugher's Bay communities. This meeting will be held at the Willard Wheatley Primary School on Thursday 22 October 2020 at 6pm. All residents of the East End and Long Look Communities are invited to attend.
FLYER: Meet the Interns	19 October	The RDA is pleased to welcome on board four interns for our first apprenticeship programme. They will be exposed to the four areas namely: 1. Procurement 2. Finance 3. Project Management 4. Environmental Management We are excited to empower our future generation through our Capacity Building Efforts.
FLYER: Tender Submission Repairs to the Attorney General's Residence	20 October	CAPTION: Important Notice Tender Submission Deadline for Repair to the Attorney General's Residence is this coming Thursday at 10:00 am. Late Submissions will not be accepted.
FLYER: RDA Contractor Workshop	20 October	CAPTION: Due to the high response to our upcoming workshop, we are hosting a second session of the Tortola Workshop which will be held on Thursday 29 October, 2020 same time same place. Seats are going fast so be sure to register before its fully booked out.
REPOST FLYER: Community Meeting Little Dix Hill, Hope Hill to Sabbath Hill to Hope Hill and Bob's Gas Station	21 October	CAPTION: See you tomorrow at 6pm.
TENDER CLOSING – Repairs to the AG's Residence	22 October	CAPTION: At today's Tender Closing we received 9 tender submissions for the Repairs to the Attorney General's Residence. The

		tenders will now go through the evaluation process and a contract will be awarded to the winning tenderer
REPOST FLYER: Community Meeting Little Dix Hill, Hope Hill to Sabbath Hill to Hope Hill and Bob's Gas Station	22 October	CAPTION: Today is the day! See you at 6pm!
RDA Apprentice Programme	26 October	CAPTION: Happening Now! Topic of Discussion: RDA Apprenticeship Programme Full interview airing tonight on "The Big Story" on JTV at 7pm.
FLYER: RDA Contractor Workshop	26 October	Workshop Presenter: Clive Petrovic Topic: Construction and the Environment
FLYER: Repairs to Anegada Administration Bulding Tender Submission Deadline	27 October	CAPTION: Important Notice: Tender Closing for the Repairs to the Anegada Administration Building tomorrow is set for at 10am. Please be reminded that late submissions will not be accepted.
TENDER CLOSING: Repairs to Anegada Administration Building	28 October	CAPTION: We are happy to announce that we have received 5 tender submissions for the Repairs to the Anegada Administration Building. The tenders will now go through the evaluation process and a contract will be awarded to the winning tenderer.
RDA Contractor Workshop	29 October	CAPTION: The RDA would like to say a big thank you to all who expressed an interest in and attended our Contractor Workshop held on Tortola. With all the positive feedback received, we can proudly say that our workshop was a success. As the construction industry continues to grow in the Territory, the RDA is committed to providing continuous training in keeping with its capacity building mandate.
Project Update: Repairs to the Road Town Police Station	30 October	CAPTION: Less than a month after K&C Construction signed the contract for the Repairs to the Road Town Police Station, not only have these works commenced but K&C Construction is ahead of schedule.

		<p>To date, progress have been made on all sections of the works listed in the scope of works.</p> <p>These are as follows:</p> <p>The existing damage chain-link fence, posts, barb-wires and curb walls on the outside of the police station have been demolished. The post foundations have been excavated and reinforcement with the formwork installed. The vertical SCH40 fence posts have been installed, aligned and casted with 4000 psi concrete.</p> <p>An office space for the maintenance supervisor which did not exist before has been erected and rendered with concrete block walls and the roof has been installed. In the Accounts Unit, drywall partitions and cubicles have been installed.</p> <p>In light of COVID -19, the road to recovery in our territory continues.</p>
<p>Signing Ceremony Deed of Contribution – Music Instruments for ESHS.</p>	<p>30 October</p>	<p>CAPTION: A Deed of Contribution signing ceremony was held today at the RDA for the contribution made by The Maples Group towards the Elmore Stoutt High School Music Department.</p> <p>The Maples Group, who have given generously in the past, gave an additional \$28K for the manufacturing of steel pan ensembles towards the ESHS School Programme.</p>

Media Coverage	Date	Description
<p>JTV: The Big Story</p>	<p>26 October</p>	<p>JTV interview Director of Strategy on the RDA Apprenticeship Programme</p>

5. Funding

The overall recovery and development programme of the RDA is funded by a combination of grants from the Government of the Virgin Islands (GoVI), the UK Government (UKG), and private funders.

The following section details contracted public funding and private grants to RDA projects to date, funding the specific initiatives listed.

Public funding is defined as funds that are granted from government or other public institutions including statutory bodies and state-owned enterprises.

Private funding is defined as funds raised from businesses, private individuals or non-governmental organisations.

The table listed below shows contracted funds. Contracted funding refers to contributions which have been fully contracted and signed by the funder. This list includes general funding for the Phase One Programme from the Government of the Virgin Islands as well as loan funding to GoVI for implementation of the Rehabilitation and Reconstruction Loan (RRL) from the Caribbean Development Bank (CDB).

Table 10: Contracted Financial Contributions by Project and Amount Contracted

Project/Initiative	Type of Funder	Amount Contracted
AO Shirley Grounds Repairs	NGO/NPO	\$75,000
AO Shirley Grounds Repairs	NGO/NPO	\$75,000
AO Shirley Grounds Repairs	NGO/NPO	\$30,000
Bregado Flax Temporary Classroom	Private Company	\$500
Bregado Flax Temporary Classroom	Private Company	\$500
Bregado Flax Temporary Classroom Refurbishment	Private Company	\$500
Construct Temporary classrooms for ESHS	NGO/NPO	\$250,000
Construct Temporary classrooms for ESHS	NGO/NPO	\$4,260
Construct Temporary classrooms for ESHS	Private Company	\$21,204
Elmore Stoutt High School (Music Classroom)	Private Company	\$100,000
Elmore Stoutt High School (Musical	Private Company	\$12,500
Elmore Stoutt High School (Musical	Private Company	\$28,000
Long Bush Recreational Facility	NGO/NPO	\$80,000
Marine Survey	Public – UKG	\$146,678
Recreation Facility on Anegada	NGO/NPO	\$60,000
Recreation Facility on Virgin Gorda	NGO/NPO	\$50,000
Repair Police Stations at Virgin Gorda	Public – UKG	\$339,799
Repair Public Administration Building (inc. Police Station) at JVD	Public - UKG	\$291,987

Special Debris Clearance	NGO/NPO	\$42,000
Special Debris Clearance	NGO/NPO	\$42,000
Special Debris Clearance	UKG	\$562,949
Temporary Housing (M&E for 15 Houses)	NGO/NPO	\$150,000
Temporary Housing (M&E for 15 Houses)	Private Individual	\$24,000
VHF trunking network design and build	UKG	\$79,966
CDB RRL Loan Programme	Public - Caribbean Development Bank via GoVI	\$43,292,488.84
Phase One Programme	Government of the Virgin Islands (GoVI)	\$10,009,200
Road Town Police Station	UKG	\$70,000
Road Town Police Station	Government of the Virgin Islands (GoVI)	\$70,000
Magistrate's Court	UKG	\$187,500
Total:		\$56,096,031.84

Alongside financial contributions, the RDA receives in-kind contributions. In-kind refers to goods and services contributed that do not involve money, such as items or services donated. To date, the RDA has contracted a total of **\$1,149,350** in in-kind contributions.

Project/Initiative	Funder Type	Value
Special Debris Clearance	UKG	\$67,600
Special Debris Clearance	UKG	\$78,000
Remove and dispose of derelict marine vessels	Private Company	\$175,000
Renewable Energy	Private Company	\$40,000
Renewable Energy	Private Company	\$20,000
Renewable Energy	Private Company	\$15,000
Strengthening of Government Asset Management	UKG	\$138,750
West End Ferry Terminal	NGO/NPO	\$225,000
Elmore Stoutt High School	NGO/NPO	\$380,000
Phase One Programme	GoVI	\$10,000
Total:		\$1,149,350

Participation by private sector and non-governmental organisations is critical to a shared, sustainable recovery and development process. This encompasses fundraising and partnerships as well as regular consultation and engagement with businesses, non-governmental organisations, and individuals in the community.

6. Project Updates – Phase One Programme

Removal of Derelict Boats	Ministry of Natural Resources, Labour and Immigration
Project: 133	Status: On Hold
Start Date: October 2018	End Date: TBD
Outcome: <i>“Improved tourism product that is aesthetically appealing, easily accessible and provides an enhanced experience to our visitors and a catalyst for economic recovery”</i>	

Overview

The passing of hurricanes Irma and Maria in 2017 left a significant number of marine vessels stranded along the coastlines and bays of the Virgin Islands. The bulk of these vessels have been removed by the owners and their insurance providers. However approximately 204 derelict vessels remain that need to be removed from their land or sea location and then disposed of.

The overall project’s procurement is currently on hold. The twelve interested tenderers who submitted tenders have officially been notified that this tender has been cancelled. We expect that a revised invitation to tender will be issued with some modifications to the Scope of Works for all Work Packages as soon as we have resolved these matters.

For reporting, we are keeping the Nanny Cay Pilot in the project update section.

Status

The final bins of fiberglass have been removed from the Paraquita Bay site to DWM Pockwood, for the pilot project.

Virgin Gorda Sports Complex

Ministry of Education, Culture,
Youth Affairs, Fisheries and
Agriculture

Project: 151

Status: Delivery

Start Date: January 2019

End Date: March 2021

Original budget: \$700,000

Cost estimate: \$1,324,203

Spend to Date: \$787,248

Outcome: *“Restored educational and recreational facilities that provide a safe and secure environment for learning and recreational activities”*

Overview

The Virgin Gorda basketball sports complex was damaged by the 2017 hurricanes and has been in a state of disrepair and thus has been unusable since then. The facility is used by the residents of Virgin Gorda for sporting events and recreation. The facility is currently unsuitable for use, denying the residents this opportunity. The scope of the project has been expanded to include a car park, outdoor court, bathrooms, and drainage improvements. Because of this, the estimated cost has been increased above.

Activity 1: Phase One, Structure and Flooring

Status: Delivery


Works to complete installation of windows, court flooring and lights continued in October, now scheduled to be completed in November, bringing phase one of this project to a close.

Activity 2: Phase Two, Bathroom, Wall, and Recycle Bins

Status: Procurement

The second phase of works to the sports complex consists of car parking, surface drainage, resurfacing of the external court and repairs to the restroom facilities. Works on the restroom facilities under phase 2 of this project continued in October.

Further elements for phase 2 of the project (parking area, sub-surface drain with soakaway system, multipurpose court) are currently undergoing detailed planning. The project's completion date has been extended to March 2021.

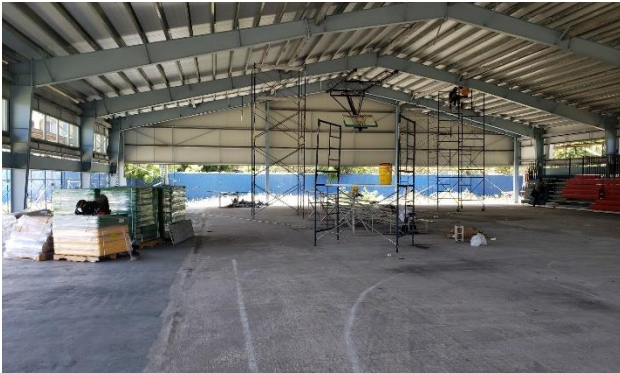

AO Shirley Grounds

Ministry of Education, Culture,
Youth Affairs, Fisheries and
Agriculture

Project: 152

Status: Delivery

Start Date: October 2018

End Date: TBD

Spend to Date: \$1,387,354

Outcome: *“Restored educational and recreational facilities that provide a safe and secure environment for learning and recreational activities”*


Overview

The AO Shirley athletics and sports grounds project is a priority project to renovate the grounds to meet international accreditation standards as an IAAF Class 2 ground, so that the Territory can host upcoming national and international events. This required preparation of the grounds prior to the installation of the new track, repairs to make the perimeter secure to boost income-generation from events, installation of bathroom facilities, installation of lights to allow events after dark, repair to the spectator stand (ideally with shade), and renovation of the clubhouse pavilion to provide meetings, events and changing facilities.

Activity 1: Track

Status: Completed

The track laying and painting have been completed, and the track activity is therefore finished. We have received feedback from BVIOC and athletes that they are happy with the quality of the track and how it was installed.

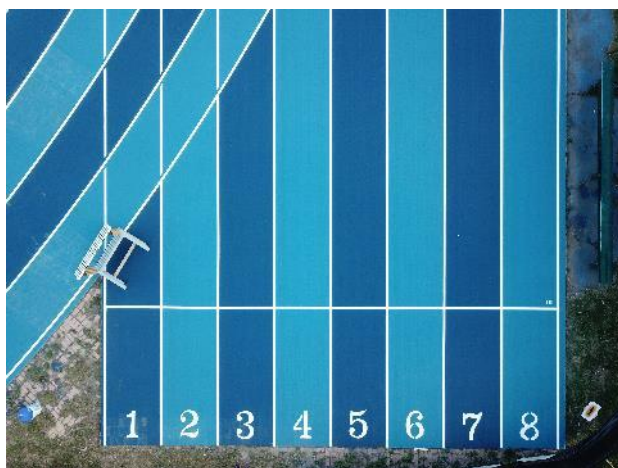

Activity 2: Bathroom

Status: Completed

The bathroom installation has been completed as of late August 2019 when final adjustments were finished.



Activity 3: Wall and Gates

Status: Completed

This activity has been completed, with all panels installed and site debris cleared on 27 November 2019. The activity was handed over to the Ministry on 5 December 2019.



Activity 4: Trackside Fence

Status: Completed

Contract was signed with No Limit Construction on 6 September. Works began and were completed in September – with completion on 30 September 2019. The trackside fence was signed over to the Ministry on 4 October 2019.

Activity 5: Lighting

Status: Delivery

In October, the delayed lighting for the grounds arrived, and installation of these lights is expected to start in November 2020.



Activity 6: Grandstand

Status: Delivery

The gym area is being focused on for completion. The gym area roof, handrails and staircases have all been installed. The seating has arrived and is being installed, to be followed by painting of the building. This activity is now scheduled to be completed in November, partly due to delays caused by the COVID curfew.

Activity 7: Pavilion

Status: On Hold

This activity has been postponed. The MECYFA are reviewing requirements and fundraising strategies.

Repair of Road Town Police Station

Governor's Group

Project: 181

Status: Delivery

Start Date: July 2019

End Date: January 2021

Original budget: \$100,000

Cost estimate: \$170,000

Spend to Date: \$26,729

Outcome: "Functioning law enforcement institutions and communication networks to restore a sense of safety and security and improved communications between agencies"

Overview

Repairs and renovations of the Road Town Police Station were implemented through the Office of the Governor, with funding from the UK Government, and the police station is now fully functional. However, some minor repairs to improve the appearance and conditions for those working within it remain outstanding.

The RDA has taken on the final repairs, including signage, fencing, painting and final office repairs, in partnership with the Deputy Governor's Office and the Royal Virgin Islands Police Force.

Status: Delivery

In October, funding was confirmed and deeds of contribution signed by both the Virgin Islands and UK Governments. October also saw award and signature of the construction contract and the commencement of works. Construction is scheduled to be completed within the next few months.



Incinerator	Ministry of Health and Social Development
Project: 186, 187, 188	Status: Delivery
Start Date: February 2019	End Date: TBD
	Spend to Date: \$218,355
Outcome: <i>“Comprehensive waste management with effective waste collection, disposal, and exportation centred around recycling.”</i>	

Overview

These are three individual projects (186, 187, and 188) that have been combined into one section for reporting purposes and in order to communicate updates more efficiently.

Part of the Department for Waste Management’s strategy for the disposal of waste products is the use of incineration to reduce the volume of waste. The incinerator used for this was decommissioned in 2011, and a new incinerator installed and commissioned. This old incinerator is still in place and needs to be disposed of as part of the infrastructure end-of-life cycle.

Project 186: Installation of Incinerator Scrubber

Status: On Hold

The installation of the new incinerator scrubber is placed on hold until the dismantling and designs are finished.

Project 187: Dismantling of the Old Incinerator

Cost Estimate: \$222,841

Status: Complete

Removal of the incinerator is complete. All other works on the site were completed on 29 May 2019. A close out report has been drafted and is being finalised.

Project 188: Install Mechanical Electrical and Plumbing (MEP) for new incinerator scrubber

Status: On Hold

The design and install MEP are currently on hold until the detailed design for the scrubber is available to commence the planning of the MEP to support the Ministry of Health and Social Development installation of the scrubber.

Marine Survey

Ministry of Natural Resources,
Labour and Immigration

Project: 189

Status: Delivery

Start Date: February 2019

End Date: TBD

Spend to Date: \$145,708

Outcome: *“The protection and prioritisation of the environment for future generations, embedding environmentally sustainable approaches to the use of the terrestrial and marine environment, including for tourism, agriculture and fisheries, and infrastructure.”*

Overview

The origins of this project were born out of discussions of BVI Government Officials’ aspirations to establish an Exclusive Economic Zone (EEZ) from the current Exclusive Fisheries Zone (EFZ). Moreover, it is envisioned that the EEZ should facilitate further development of the Blue Economy. In July 2017, the Ministry of Natural Resources, Labour and Immigration convened a workshop where various partners which included the National Oceanography Centre (NOC), as well as private sector stakeholders were in attendance. The body understood that the formulation of a National Ocean Policy underpinned by a marine spatial plan would set the framework in which the Blue Economy would be implemented.

The NOC advised on the range of capabilities it could render to perform the acquisition of data to inform planning, policy and strategic objectives.

Activity 1: Capacity Building

Status: Complete

The National Oceanography Centre (NOC) was engaged to deliver the following: 1) Undertake survey capacity building through the surveying of a biodiverse marine area, focussing on ground truthing of existing data. 2) Capacity Building to transfer skills in mapping marine habitats using modern acoustic survey tools. 3) Provide recommendations of a suite of marine survey equipment (both manual and autonomous techniques) suitable for local staff to undertake marine surveys to meet the objectives.

The attendees of the capacity building activity were mainly from departments under the Lead Ministry, the Ministry of Natural Resources, Labour and Immigration, with representation from other departments and statutory agencies whose work involves the marine sector. Additionally, representatives from non-governmental organizations also were recipients of the training.

Activity 2: Equipment Purchase

Status: Complete

All equipment has been delivered and a handover was held on 7 February 2020 at the RDA office.

Activity 3: Marine Data Framework: Technical Assistance

Status: Delivery (COVID dependent)

Two stakeholder meetings were held in November in order to finalize the ToR for technical assistance and a final meeting was held on 24 January 2020.

A single source procurement of technical assistance has been approved and the contract is currently being drafted and reviewed. The UK National Oceanography Centre is expected to undertake stakeholder engagement, assessment of data and scientific products, and deliver additional training. There were plans for UK NOC to visit in March, however this was postponed by MNRLI. The visit will most likely be rescheduled to November 2020. Until then, remote work and training methods will be utilised.

As of July, the close out report for completed activities have been finalized and a follow up meeting is being held between UK NOC and MNRLI. The team is currently reviewing the feasibility of remote stakeholder engagements as well as possibly applying for further funding.



7. Project Updates – CDB Programme

Magistrate’s Court	Premier’s Office
Project: 060	Status: Planning
Start Date: March 2020	End Date: August 2022
Outcome: <i>“Improved climate resilient and socially-inclusive infrastructure and institutions in the transport, water and sewerage, governance, education and national security sectors in the Virgin Islands.”</i>	

Overview

This project is focused on the first phase of redevelopment of the territories’ legal infrastructure, by constructing a magistrate’s court on the old Eslin Henley site in Tortola. It aims to complete the process of ensuring continuity of the judicial process throughout the natural disasters experienced, by relocating the magistrate’s court occupants from their temporary facility.

Status

Deputy Governor’s Office’s approval of the Inception and Environmental and Social Management reports was secured in late September. In October, RDA held discussions with the design consultant Trojan and the DGO on scaling the project requirements based on the available budget. This will need to be agreed prior to procurement of construction.

Eslyn Henley Richez Learning Centre	Ministry of Education, Culture, Youth Affairs, Fisheries and Agriculture
Project: 083	Status: Planning
	End Date: TBD
Outcome: <i>“Improved climate resilient and socially-inclusive infrastructure and institutions in the transport, water and sewerage, governance, education and national security sectors in the Virgin Islands.”</i>	

Overview

This project is to construct a new facility for the Eslyn Henley Richez Learning Centre, which is a Special Educational Needs facility, taking a holistic approach to the reconstruction. A facility to serve up to thirty students which is fully disabled accessible and accommodates the needs of students who are severely autistic, mentally as well as physically challenged, and may have a variety of learning disabilities.

Status

The Ministry has confirmed agreement with the recommended option presented in the final Inception Report, and the consulting firm has been instructed to proceed with the preliminary design based on the recommended option. In October several environmental issues were highlighted which will be incorporated in the preliminary design.

Bregado Flax Educational Centre

Ministry of Education, Culture, Youth Affairs, Fisheries and Agriculture

Project: 086

Status: Delivery

End Date: TBD

Cost Estimate: \$1,695,727.56

Spend to Date: \$427,667

Outcome: *“Improved climate resilient and socially-inclusive infrastructure and institutions in the transport, water and sewerage, governance, education and national security sectors in the Virgin Islands.”*

Overview

This project is to undertake the rehabilitation of existing Blocks 2-4 and the Administration Block of the Bregado Flax Educational Centre. This project is aimed not only at rehabilitating the existing hurricane-damaged buildings, but also adding resilience through the installation of a concrete roof.

Status

In October the steel formwork and concrete pouring for one of the classroom building’s roof was completed. The contractor’s proposed variations have been submitted and are currently under review.



West End Ferry Terminal

Project: 091

Start Date: April 2019

Premier's Office

Status: Planning

End Date: TBD

Outcome: *“Improved climate resilient and socially-inclusive infrastructure and institutions in the transport, water and sewerage, governance, education and national security sectors in the Virgin Islands.”*

Overview

The West End Ferry Terminal has been an important mode for travellers moving between the British Virgin Islands and the US Virgin Islands, as well as the sole hub for domestic travel between Jost Van Dyke and Tortola. This is a major access hub to the Virgin Islands with 170,000 passengers routing through this terminal in 2016. The destruction of the facility during hurricanes Irma and Maria has presented challenges to travellers wishing to travel to the BVI.

The West End Ferry Terminal project aims to revitalize the terminal and enhance it to be a major port hub within the Virgin Islands.

Status

The withdrawal of donor funding means this project will now be entirely financed by CDB. The changes to the funding arrangement have led to a wider review of the project implementation strategy which is currently being conducted, with a view to issuing an expression of interest (EOI) for a design and construction supervision consultant.

The evaluation report for the Expressions of Interest (EOI) for the Consultant who will oversee the project has been submitted to the CDB for its no objection, following which a contract will be issued to the selected firm.



Reservoirs and Metering

Ministry of Transportation, Works and Utilities

Project: 140

Status: Delivery

Start Date: October 2019

End Date: November 2020

Cost Estimate: \$4,722,736

Spend to Date: \$1,449,629

Outcome: *“Improved climate resilient and socially-inclusive infrastructure and institutions in the transport, water and sewerage, governance, education and national security sectors in the Virgin Islands.”*

Overview

Hurricanes Maria and Irma caused damage to the water and sewage system estimated at around \$63,000,000. There was severe damage to the water network and major storage reservoirs were all impacted to various extent. From minor impact to completely destroyed assets, the two hurricanes left a severely compromised infrastructure. The average level of un-accounted for water after the hurricanes stands over 50% and this comprises both physical and commercial losses.

Most of the water distribution network was impacted by the Hurricane leading to water leaks in the water supply network. The customer metering coverage is partially restored, with the rest of the customers being on assessed consumption. The Government has taken a holistic approach to the rehabilitation and reconstruction of the damaged infrastructure.

Current Status

Autland Construction is proceeding with site work on two sites, with a 30-day contract extension granted due to weather and COVID-19 delays.

Carrot Bay site: Progress has continued on site and both the upper and lower concrete retaining walls have been completed and backfilled.

Long Bush site: The steel and concrete work for the lower section of the retaining wall is in progress.

Zion Hill site: The current reservoir must remain in full operation until the Carrot Bay reservoir has been constructed, tested and commissioned. This was not envisioned at the start of the project but is the only way to ensure water supply to local residents is not interrupted.



Roads, Slopes, and Coastal Defences

Ministry of Transportation, Works, and Utilities

Project: 180

Status: Delivery

Start Date: January 2020

End Date: May 2021

Spend to Date: \$6,435

Outcome: *“Improved climate resilient and socially-inclusive infrastructure and institutions in the transport, water and sewerage, governance, education and national security sectors in the Virgin Islands.”*

Overview

The intended goal of this project is to repair, rehabilitate and reconstruct the priority roads in the Territory. There was severe damage to the road network on the western and north western portion of Tortola. Sea defences in different areas were destroyed and will require replacement and upgrading. Other roads suffered significant damage down to the sub-grade beneath the concrete layer, while in other areas rehabilitation works will include road/slope/embankment stabilization.

Current Status

Site work on the Great Mountain 1 site continued in October. The retaining wall including weep holes and geotextile fabric has been completed and backfilled. Four contract signings for this project were held in October, namely the Great Mountain 2 site, the Ballast Bay/Windy Hill site, Bob’s Gas Station, and Little Dix Hill. The final two packages will be initiated once the preceding works are completed, in order to ensure traffic flow into and out of Road Town is maintained.



Other Government Buildings

Project: 200

Start Date: April 2020

Cost Estimate: \$3,011,671

Deputy Governor's Office

Status: Delivery

End Date: June 2021

Spend to Date: \$968,859

Outcome: "Improved climate resilient and socially-inclusive infrastructure and institutions in the transport, water and sewerage, governance, education and national security sectors in the Virgin Islands."

Overview

There are three Government Buildings in Virgin Gorda, that will be completely refurbished under the Caribbean Development Bank's Recovery and Rehabilitation Loan. The \$3.3m project will include the rehabilitation of Vanterpool, Flax and North Sound complexes. The objective of the project is to restore the functionality of the administrative heart of Virgin Gorda, whilst adding resiliency and functionality to the spaces. A series of local contractors will complete the package of works, and the project is set to commence construction in May 2020, pending the lifting of BVI COVID-19 restrictions.

Status

Work continues on both the Flax and North Sound contracts:

North Sound Building

The North Sound Building works are progressing, now scheduled to be completed by the end of November, following COVID-19 delays.

Flax Building

Work on the Flax Building contract remains on track despite some COVID-19 delays. The new roof has been installed, and drywall, electrical work and tiling work is nearing completion.



Vanterpool Building

The Vanterpool building contract was signed on 15 October, and the contractor is expected to have full access to the building from 15 November.

8. Completed Projects

Incinerator Dismantling	Ministry of Health and Social Development
Project: 187	Start Date: February 2019
Planned Completion Date: December 2019	Actual Completion Date: June 2020
Original budget: \$175,000 Cost estimate: \$222,841	Spend to Date: \$209,885.92
Outcome: <i>“Comprehensive waste management with effective waste collection, disposal, and exportation centred around recycling.”</i>	

Summary Report

The Incinerator Dismantling project began in February 2019, aimed at dismantling the old incinerator in Pockwood Pond, Tortola, freeing required space for implementation of additional, more modern waste management solutions.

The old incinerator had been decommissioned since 2011 but was never dismantled and disposed of. As such, the RDA was tasked with dismantling the incinerator through this project, thereby creating space required for additional waste management solutions to be implemented in the Territory.

This project was able to deliver on its planned outputs, disposing of the old incinerator and thus creating 2,704 square feet of space within the Incinerator Complex in Pockwood Pond.

Success of this project is closely linked with and facilitates the implementation of the Territory’s wider waste management strategy.

A Value for Money report for this project is currently being drafted and will be released shortly.



8.1. Past Completed Projects

Projects that have been completed for more than three months are archived and included below with their Value for Money assessment scores.

Each project completed by the RDA undergoes a Value for Money (VfM) assessment using the RDA's VfM Framework. The VfM framework measures a project's Economy, Efficiency, Effectiveness and Equity. The assessment assigns an overall VfM score out of 100 to each project evaluated. VfM Scores and Reports detailing performance are referenced in the Table below.

Project Code	Project	Month of Completion	Overall VfM Score	VfM Report
187	Incinerator Dismantling	June 2020	TBD	
136	Sea Markers	June 2020	80/100	Sea Markers VfM Report
154	Temporary Homes	March 2020	50/100	Temporary Homes VfM Report
145	BFJS Internal Walls	January 2020	TBD	
103	Virgin Gorda Baths	January 2020	TBD	
157	Repair to Damaged Homes	January 2020	70/100	Repair to Damaged Homes VfM Report
147.01	ESHS Temporary Classrooms	September 2019	80/100	ESHS Temporary Classrooms VfM Report
147.02	ESHS CTL Improvements	August 2019	70/100	ESHS CTL Improvements VfM Report
182	Virgin Gorda Police Barracks Repair	July 2019	78.9/100	VG Police Barracks VfM Report
183	Jost Van Dyke Admin Building Repair	August 2019	65.0/100	JVD Admin Building VfM Report
146	ESHS Demolition	June 2019	100/100	ESHS Demolition VfM Report
108	Special Debris Clearance	April 2019	64.7/100	Special Debris Clearance VfM Report
